

Agile Scrum Development in an *ad hoc* Software Collaboration

A. L. Baxter,^{1, a} S. Y. BenZvi,² W. Bonivento,³ A. Brazier,⁴ M. Clark,¹ A. Coleiro,⁵ D. Collom,⁶ M. Colomer-Molla,^{5, 7} B. Cousins,^{8, 9, b} A. Delgado Orellana,¹⁰ D. Dornic,¹¹ V. Ekimtcov,¹² S. ElSayed,¹³ A. Gallo Rosso,¹⁴ P. Godwin,^{15, 9} S. Griswold,² A. Habig,¹⁶ S. Horiuchi,¹⁷ D. A. Howell,^{6, 18} M. W. G. Johnson,¹² M. Jurić,^{19, 20} J. P. Kneller,²¹ A. Kopec,¹ C. Kopper,²² V. Kulikovskiy,²³ M. Lamoureux,²⁴ R. F. Lang,¹ S. Li,¹ M. Lincetto,¹¹ W. Lindstrom,⁶ M. W. Linvill,¹ C. McCully,⁶ J. Migenda,²⁵ D. Milisavljevic,¹ S. Nelson,¹⁹ R. Novoseltseva,²⁶ E. O'Sullivan,²⁷ D. Petravick,¹² B. W. Pointon,^{28, 29} N. Raj,²⁹ A. Renshaw,³⁰ J. Rumleskie,¹⁴ R. Tapia,^{8, 9} J. C. L. Tseng,³¹ C. D. Tunnell,^{32, 33} C. F. Vigorito,³⁴ C. J. Virtue,¹⁴ C. Weaver,²² L. Winslow,³⁵ R. Wolski,¹³ X. J. Xu,³⁶ and Y. Xu³²

(The SCiMMA and SNEWS Collaborations)

¹*Department of Physics and Astronomy, Purdue University, West Lafayette, IN 47907, USA*

²*Department of Physics and Astronomy, University of Rochester, Rochester, NY 14627, USA*

³*INFN sezione di Cagliari Istituto Nazionale, Complesso Universitario di Monserrato - S.P. per Sestu Km 0.700, I-09042 Monserrato (Cagliari), Italy*

⁴*Center for Advanced Computing, Cornell University, Ithaca, NY 14853, USA*

⁵*Université de Paris, CNRS, AstroParticule et Cosmologie, F-75013, Paris, France*

⁶*Las Cumbres Observatory, Goleta, CA 93117, USA*

⁷*Instituto de Física Corpuscular (CSIC - Universitat de València) c/ Catedrático José Beltrán, 2 E-46980 Paterna, Valencia, Spain*

⁸*Institute for Computational and Data Sciences, The Pennsylvania State University, University Park, PA 16802, USA*

⁹*Department of Physics, The Pennsylvania State University, University Park, PA 16802, USA*

¹⁰*Pontificia Universidad Católica de Chile, Santiago, Región Metropolitana, Chile*

¹¹*Aix Marseille Univ, CNRS/IN2P3, CPPM, Marseille, France*

¹²*National Center for Supercomputing Applications,*

University of Illinois at Urbana-Champaign, Urbana, IL 61801, USA

¹³*Department of Computer Science, University of California Santa Barbara, CA 93106, USA*

¹⁴*Department of Physics, Laurentian University, Sudbury ON P3E 2C6, Canada*

¹⁵*Institute for Gravitation and the Cosmos, The Pennsylvania State University, University Park, PA 16802, USA*

¹⁶*Department of Physics and Astronomy, University of Minnesota Duluth, Duluth, MN, 55812, USA*

¹⁷*Center for Neutrino Physics, Department of Physics, Virginia Tech, Blacksburg, VA 24061, USA*

¹⁸*University of California Santa Barbara, CA 93106, USA*

¹⁹*DiRAC Institute, University of Washington / Rubin Observatory, Seattle, WA, USA*

²⁰*Department of Astronomy, University of Washington / Rubin Observatory, Seattle, WA, USA*

²¹*Department of Physics, NC State University, Raleigh, NC 27695, USA*

²²*Department of Physics and Astronomy, Michigan State University, East Lansing, MI 48824, USA*

²³*INFN Sezione di Genova, Via Dodecaneso 33, Genova, 16146 Italy*

²⁴*INFN Sezione di Padova & Università di Padova, Dipartimento di Fisica, Padova, Italy*

²⁵*Department of Physics, King's College London, London WC2R 2LS, UK*

²⁶*Baksan Neutrino Observatory, Institute for Nuclear Research of Russian Academy of Sciences, Neytrino, Kabardino-Balkarian Republic, Russia, 361609*

²⁷*Department of Physics and Astronomy, Uppsala University, Box 516, S-75120 Uppsala, Sweden*

²⁸*Department of Physics, British Columbia Institute of Technology, Burnaby, BC, V5G 3H2, Canada*

²⁹*TRIUMF, Vancouver, BC V6T 2A3, Canada*

³⁰*Department of Physics, University of Houston, Houston, TX 77204, USA*

³¹*Department of Physics, University of Oxford, Keble Road, Oxford OX1 3RH, UK*

³²*Department of Computer Science, Rice University, 6100 Main St, Houston, TX, 77005, USA*

³³*Department of Physics, Astronomy, Rice University, 6100 Main St, Houston, TX, 77005, USA*

³⁴*Department of Physics, University of Torino & INFN, via Pietro Giuria 1, 10125 Torino, Italy*

³⁵*Massachusetts Institute of Technology, Cambridge, MA 02139, USA*

³⁶*Université Libre de Bruxelles, 1050 Bruxelles, Belgium*

Developing cyberinfrastructure for the growing needs of multi-messenger astrophysics requires expertise in both software development and domain science. However, due to the nature of scientific software development, many scientists neglect best practices for software engineering which results in software that is difficult to maintain. We present here a mitigation strategy where scientists adopt software development best practices by collaborating with professional software developers. Such a partnership brings inherent challenges. For the scientists, this can be a dependence on external resources and lack of control in the development process. For developers, this can be a reduction in effort available for core, non-scientific development goals. These issues can be alleviated by structuring the partnership using established software development practices, such as the Agile Scrum framework. This paper presents a case study wherein a scientist user group, the SuperNova Early

Warning System (SNEWS), collaborated with a group of scientific software developers, the Scalable Cyberinfrastructure for Multi-Messenger Astrophysics (SCiMMA) project. The two organizations utilized an Agile Scrum framework to address the needs of each organization, mitigate the concerns of collaboration, and avoid pitfalls common to scientific software development. In the end, the scientists profited from a successful prototype and the software developers benefited from enhanced cyberinfrastructure and improved development skills. This suggests that structured collaborations could help address the prevailing difficulties in scientific computing.

I. INTRODUCTION

There are inherent difficulties for software development in scientific computing. Scientists spend about 30% of their time developing scientific software and often learn the tools they need during the development process [1, 2]. This is because the culture of scientific research emphasizes publishing papers rather than publishing code [3]. Scientists develop software in order to sustain short timelines, focus on papers, and follow changing scientific questions. They quickly develop software in order to study the science [4], rather than produce a finalized software product. This culture of scientific computing may cause some scientists to neglect best practices in software engineering. These include using high-quality open-source software and using version control and issue tracking tools [5]. These difficulties have been described as a “chasm” between scientific computing and formal software development [6, 7].

This chasm can be mitigated if scientists adopt software engineering best practices, either by learning and integrating the practices themselves or by collaborating with professional software developers [7]. The latter option is useful because the scientists can use their domain expertise to explain software requirements to the software developers, allowing the two groups to utilize their collective knowledge to generate proper protocols, tests, and functions from the scientific use-case [8]. However, there are some inherent challenges in such a partnership. For the scientists, this can include building a reliance on external code, difficulty in communicating their evolving needs to the developers, and ensuring timely completion of development goals. For software developers, this can be a reduction in effort available for development goals not specific to any science effort, ensuring timely progress on other development projects, and difficulty in understanding the scientists’ domain-specific language. One approach to mitigate these issues is the Agile Scrum software development framework [7, 8]. The Agile framework is an iterative approach to software development, wherein short-term development tasks (weeks to months) are favored over large, long-term goals for the end product [9, 10]. Agile’s emphasis on short-term development goals might not seem reasonable for large-scale scientific projects, such as the SuperNova Early Warning

System or the Large Synoptic Survey Telescope, as these projects often have long-term science goals on the order of decades [11, 12]. But, for a single software project within the big science picture, Agile methods could be suitable. Agile practices manifest as incremental development tasks (“user stories”) completed while in an active dialogue with users to discover emergent software requirements [10]. The Scrum approach is one method to adopt Agile practices into a project [8, 10]. Scrum is a process framework that structures a project into a planning phase, design phase, and development phase (a “sprint”), which matches Agile’s incremental and emergent approach to software development [13]. These incremental and emergent elements are particularly relevant in the scientific computing software development communities given their evolving software requirements and frequent need for rapid results [8, 14–17]. However, Agile methods tend to be rarely implemented [6, 7, 18] or incorrectly followed [8] in the scientific computing community.

In light of these difficulties, we present a case study where a science user group collaborated with software developers and successfully utilized Agile Scrum practices to mitigate pitfalls common to scientific software development. The nature of this collaboration introduced additional complications for the software developers who were not devoted to exclusively supporting the science user group. Instead, the developers were committed to providing scientific software services for a range of users, rather than the specific needs of this one user group. These issues included: supporting the user group without derailing core development, staying in-sync with the user group development, and supporting operational infrastructure during the development of their software client. These difficulties were circumvented by emphasizing the iterative and emergent elements in the Agile Scrum methodology implemented for the collaboration.

An overview of the two groups involved is provided in Section II. The software development resulting from the collaboration is described in Section III, with the Agile Scrum structure of the collaboration in Section IV. Finally, Section V reviews the collaboration and provides key takeaways applicable to the general collaborative scientific programming community given the difficulties it faces.

^a SNEWS corresponding author: adepoian@purdue.edu

^b SCiMMA corresponding author: bfc5288@psu.edu

II. ORGANIZATIONS

The SuperNova Early Warning System (SNEWS) is an open, public alert system that is built to provide an early warning for core-collapse supernova in the close-by Universe [19]. The first indication of a potential stellar explosion will be the arrival of a burst of neutrinos [20]. If several detectors report a potential supernova within minutes, SNEWS will issue an alert to its subscribers which include astronomical observatories, neutrino detectors, and amateur astronomers and citizen scientists. There are seven neutrino experiments participating in the current SNEWS framework. There are about 20 neutrino detectors worldwide that are planned to participate in the new SNEWS 2.0 framework. Each of these neutrino detectors have individual data readouts, from which the SNEWS framework must be able to identify likely neutrino burst events. Additionally, these neutrino detectors will be active within SNEWS at different times. With these specific requirements, SNEWS is one of the few successful examples to date of cyberinfrastructure spanning major neutrino experiments [12]. In the current era of multi-messenger astrophysics (MMA) there are new opportunities for SNEWS to optimize its science reach for the next Galactic supernova. To achieve this goal, SNEWS depends on developing and sustaining software with a number of integrated components [12].

SNEWS represents one agent in an ever-growing community of MMA organizations that rely heavily on cyberinfrastructure to support their science requirements [11, 21–27]. The cyberinfrastructure requirements for this community are similarly growing, given the need for prompt, reliable, and efficient alerting at scale, and for coordination between MMA organizations that use differing message conventions and formats [27–30]. These requirements span multiple detectors, institutes, and nations, and would be very intensive for any individual group to provide [31]. These difficulties prompted the creation of the multi-institute Scalable Cyberinfrastructure for Multi-Messenger Astrophysics (SCiMMA) project. SCiMMA has been addressing the cyberinfrastructure needs of the MMA community by engaging with MMA organizations [32, 33], developing a multi-format MMA data distribution software client [34], and providing server infrastructure to support MMA data distribution [35]. To develop these services, SCiMMA has utilized an Agile Scrum framework and has established best-practices for scientific software development [36], including: open-source version control and issue tracking using Github, maintaining a branching and pull request development framework, source documentation, configuration management via containerization, software testing via Pytest, continuous integration, and a formal, automated release process [34, 37].

While both SNEWS and SCiMMA have already developed substantial cyberinfrastructure, each group was looking to make several improvements. SNEWS was seeking a software client and network infrastructure to

prototype a modernized data distribution platform for the SNEWS 2.0 framework and had designed software requirements, but it was seeking further resources for software and infrastructure development [12]. SCiMMA was seeking to directly support the MMA community and had assessed the community’s broader cyberinfrastructure needs, but was searching for practical use-cases and requirements for its software and server infrastructure [31].

A member of SNEWS, who is also a principle investigator for DIDACTS [38], connected with SCiMMA at a National Science Foundation “Harnessing the Data Revolution” grant meeting [39]. Together, they proposed an informal cooperation between SNEWS and SCiMMA given the clear overlap of interests. The cooperation began without direct collaboration between the groups (Phase 0 in Figures 1 and 2), where SNEWS carried out its own code development using SCiMMA code publicly available on Github [34]. Later, the partnership evolved into a larger collaboration (Phases 1 and 2 in Figures 1 and 2) involving both SNEWS and SCiMMA developers. This ultimately catalyzed development for both organizations, but it began with inherent risks due to the collaboration’s spontaneous nature and the pre-alpha status of each group’s cyberinfrastructure. For SNEWS, the main question was: “can we accomplish our scientific goals while relying on a common, externally-supported cyberinfrastructure solution to aid the long-term sustainability of our systems?” For SCiMMA, the main question was: “would diverting from our core development effort be feasible and worthwhile given our constrained timeline and need to progress on other projects?”

These issues were addressed through an active two-sided collaboration coordinated with Agile Scrum methods. The nature of the collaborative development (Section III) and the project management (Section IV) were each essential to address the constraints and concerns of each organization.

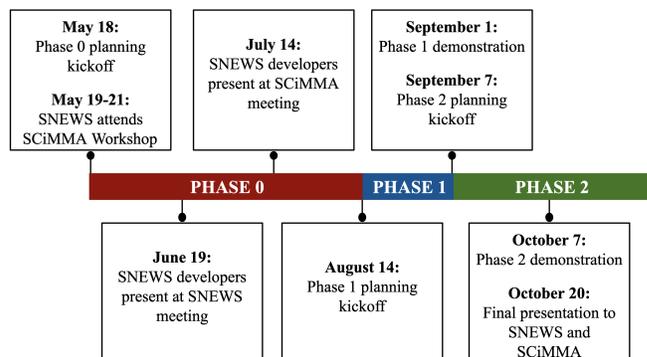


FIG. 1. Timeline of events that led to the development of the SNEWS-SCiMMA collaboration and the SNEWS 2.0 prototype.

Phase 0	Phase 1	Phase 2
May 18 - August 14	August 14 - September 7	September 7 - October 20
Goal: Prototype SNEWS 1.0 using the hop-client	Goal: Test prototype components locally	Goal: Test prototype components remotely
Outcome: Prototype working with initial publishing, subscribing, and decision making frameworks	Outcome: Prototype working with distributed components via local installations and containerized servers	Outcome: Prototype working with distributed components via remote installations and cloud servers

FIG. 2. Illustration of the three phases that progressed during the SNEWS-SCiMMA collaboration. Outlined are the goals and outcomes from each phase. Each phase proceeded only after a consensus between organizations. The conclusion of each phase marked an evaluation period for each organization, which provided a decision point on whether to continue the collaboration. This was essential to ensure the collaboration was addressing the emergent needs and perspectives of each organization.

III. COLLABORATION DEVELOPMENT

SNEWS was looking to upgrade their alert software framework from the current version of SNEWS to SNEWS 2.0. SNEWS 2.0 would require a scalable and reliable publish-subscribe system with potentially cloud-based services. SNEWS could either build these systems from scratch, or rely on existing software and systems. Each option would offer advantages, but also present challenges. Option 1, building from scratch, puts the development, support, and maintenance burden all on SNEWS developers. While the SNEWS scientists are skilled in scientific computing, they lack extensive experience with formal software engineering. Option 2, using an open-source publish-subscribe system, would require SNEWS to update its software when the underlying open-source goes through a release cycle. Open-source projects are often not backward compatible. SNEWS would be held responsible for changes made by the open-source development team upstream which SNEWS depends on. Option 3, using a cloud-based service, does not offer any customization options and while it might be affordable at the present time, there would be no way to ensure that future costs would not obsolete the system. A new option, Option 4, arose wherein SNEWS could work with a development team that was already attempting to mitigate the risks of a publish-subscribe system. SCiMMA was developing HOPSKOTCH [34], a system involving a stand-alone publish-subscribe system and as a hosted cloud service. It is based on an open-source platform, but it provides its own application programming interface (API) to preserve functionality in case of changes to the current internal system, Apache Kafka [40]. This insulates the users of HOPSKOTCH from the backward compatibility risks of open-source software. Moreover, the HOPSKOTCH development team includes professional software engineers who

are trained to implement, maintain, and support features as part of their software system.

Upon learning about SCiMMA and their HOPSKOTCH software and infrastructure, SNEWS considered to test development of their software prototype using this publish-subscribe system. This allowed SNEWS to use resources provided from SCiMMA to kickstart the initial development. However, SNEWS was concerned about relying on external software since there could be diverging development priorities between the organizations, which could result in missing features. Moreover, the resulting software could become a complex black box for SNEWS if they were not engaged in the development process. Nonetheless, SCiMMA’s available features and end goal appeared to fit all of their needs, so SNEWS decided to proceed.

SNEWS carried out the initial development which began in Phase 0 (Figure 2). During this stage, SNEWS developers attended the SCiMMA 2020 Virtual Workshop software demonstration session [33]. This allowed the SNEWS developers to utilize the SCiMMA hop-client application template as the basis for their SNEWS 2.0 prototype using the current software requirements of SNEWS. They extended the template with additional, SNEWS-specific functionality, maintaining the codebase in a private Github repository and running local tests in Python. During development, SCiMMA added the SNEWS developers to the SCiMMA Slack to provide user support and debugging as SNEWS developed the prototype. The development itself was driven entirely by SNEWS. This phase was successful in re-deployment of SNEWS functionality with hop-client, but there were key elements missing, such as data storage and experiment authentication. SNEWS provided SCiMMA with a status update at SCiMMA’s July 2020 Public Teleconferences (Figure 1), highlighting the current implementation, usage requirements, and features desired by SNEWS not currently in SCiMMA’s software [41].

This prompted a period of internal assessment for SCiMMA to evaluate the feasibility and utility of collaborating with SNEWS. The potential benefits of a collaboration were promising, as SNEWS would serve as SCiMMA’s first concrete use-case and provide practical requirements for its cyberinfrastructure. SCiMMA proposed a short period of focused development with SNEWS near the end of Phase 0. However, this presented a risk to SCiMMA’s core goals given its limited number of developers. To mitigate this and ensure that development would not be derailed, the SCiMMA team formally integrated the collaboration into its own Agile sprint structure. The team created a primary deliverable goal, an “Epic”, which generated user stories specifically for SNEWS development support and assigned it to two developers [42]. During Phase 0, the two SCiMMA developers remained active in the core SCiMMA development and assessed the SNEWS codebase but did not commit any time towards SNEWS software development. After SNEWS’s presentation to SCiMMA and the SCiMMA

developers’ internal sprint presentation (Figure 1), it became clear that providing SNEWS with software and expertise would support SNEWS’s development goals while providing an informative use-case for SCiMMA’s own development. While there were still concerns about allocating effort away from core development, SCiMMA proposed a short period of focused collaboration with SNEWS (Phase 1) given the many synergies between the projects. Both groups then decided to actively work together to further the development of the SNEWS 2.0 prototype.

Given the concerns of each organization, the structure of the collaboration would need to meet several constraints. First, the workload would need to be shared between organizations. This would avoid software duplication, ensure that SNEWS would have the understanding required to sustain the codebase after SCiMMA’s involvement, and allow the SCiMMA developers to understand the existing codebase on a short timescale. Second, the software requirements would need to be rapidly and iteratively communicated by SNEWS and evaluated by SCiMMA. And third, the SNEWS-specific development would need to be balanced with SCiMMA’s core development goals. The iterative and emergent nature of these constraints, along with their short timescale, suggested that an Agile Scrum framework would benefit the collaboration.

IV. COLLABORATION STRUCTURE

Given the concerns and constraints of the SNEWS and SCiMMA organizations, a structured approach to the collaboration was essential. The two-week period of focused collaborative development (Phase 1 of Figure 2) provided informative requirements for the collaboration structure, which evolved into more formal project management structures in the longer Phase 2.

A. Addressing limited resources

As the Phase 1 collaboration began, SCiMMA created an Epic for a collaborative “mini-sprint” with SNEWS, and the two developers focused full effort on the Epic. SCiMMA integrated this coding sprint into the regular SCiMMA Agile Scrum status updates during daily check-ins and sprint reviews; ensuring that the collaboration would remain in-line with core development. This provided an active dialogue throughout Phase 1, allowing SCiMMA to remain in-sync and prepared to flexibly adjust its development plans as needed. This dialogue made it clear that the collaboration was benefiting core SCiMMA development as multiple new user stories were generated from bugs discovered and features requested during Phase 1. Discussions of these user stories during SCiMMA sprint reviews indicated that these requests were of general MMA interest, suggesting that the

SNEWS use-case was driving SCiMMA’s software development and aligning with its goal to support the MMA community.

B. Addressing communication & reliance on external software

While the Phase 1 goals had already proved useful for core SCiMMA development, the goals alone did not address SNEWS’s concerns of relying on external software and having their features and bugs represented in SCiMMA’s sprint planning. Instead, these concerns were addressed by the structure of the collaboration itself. One SCiMMA developer proposed that the two teams adopt an Agile Scrum structure based on SCiMMA’s development framework, so that Phase 1 would be a short-term collaborative “mini-sprint.” The teams agreed, and the developer took the role of “scrum master” by coordinating meetings and organizing user story creation. Developers from each team actively engaged in the mini-sprint, which was structured around regular communication via Slack and project management via a GitHub project board. Informal coding sprint meetings were set up in parallel with SCiMMA’s ongoing sprint meetings, with virtual pair-programming sessions between SNEWS and SCiMMA for *ad hoc* code debugging and technical questions.

This framework ensured bilateral effort for the collaboration and provided regular communication between the organizations. It gave SNEWS an active role in the development, allowing for feature requests and bugs to be relayed through the SCiMMA developers to the ongoing SCiMMA sprint. This also allowed for SNEWS to become familiar with the software which would mitigate the potential risk of software sustainability after the collaboration. The Agile Scrum framework also supported timely development by allowing large goals to be translated into smaller tasks, promoting iterative development.

C. Addressing timeline constraints

Phase 1 concluded with a demonstration of the software to the SNEWS and SCiMMA stakeholders. After reviewing the collaboration progress, it was clear that there was mutual benefit without the initial concerns. Both organizations agreed to a second, four-week period of focused development (Phase 2 of Figure 2). However, at the end of Phase 1, there were clear timeline constraints: SNEWS was seeking to begin productionizing the software and SCiMMA was looking to dedicate more effort to core development tasks resulting from the collaboration.

To address these timeline pressures, the collaboration was re-structured in Phase 2 to follow a more formalized sprint format. More detailed and clearly defined user sto-

ries were tied back to the Epics in order to kickoff the collaboration, sprint meetings were scheduled in advance at regular intervals, and sprint check-ins were reformatted as a round-table through all developers to ensure comprehensive progress updates. This revised format was a useful means to continue Agile Scrum development, as the short-term, iterative development progress could be checked against the longer-term Epics during each sprint. This allowed for both the user stories and the Epics themselves to be revised based on emergent developer input and promoted the involvement of all members. The user stories were revised to include more intense coding sprints in order to add additional features to the prototype.

As with Phase 1, Phase 2 concluded with a demonstration of the software to the stakeholders. The demonstration was recorded as an endpoint marking the conclusion of the intense software development period [43].

V. CONCLUSION

By forming a collaboration with SCiMMA’s software developers, SNEWS mitigated various difficulties inherent to scientific software development. The emerging risks of the collaboration were alleviated by implementing practices from the Agile Scrum software development framework. Within this framework, the two organizations collaborated to successfully produce a prototype of SNEWS 2.0 using SCiMMA’s hop-client publish-subscribe system [44]. By working in coding sprints, the high-level goals of each organization were translated into manageable development tasks. This allowed for the project to proceed within the constrained timeline while also addressing the concerns specific to each organization. The iterative development process led to sustainable software development by ensuring a bilateral effort from both teams. The collaboration was mutually beneficial. SCiMMA utilized SNEWS’s practical use-case to further its software and infrastructure to support the broader MMA community. SNEWS gained a functional and maintainable prototype of their desired software while also gaining valuable software development experience. The collaboration allowed both organizations to gain useful experience and new knowledge to progress their science programs individually and collectively using Agile Scrum development techniques.

This case study supports the basis that scientists can benefit from collaborating with software developers to help bridge the chasm between scientific software and software engineering. Moreover, it suggests that such a collaboration can be mutually beneficial, especially if the software developers are serving a broader community of scientists. Additionally, a collaboration of this nature can prove particularly useful even when the software products are not themselves finalized, since it can provide concrete use-case requirements to help shape software development. This benefit is particularly powerful if the collaboration structure promotes emergent and iterative

progress, as is the case within management systems such as the Agile Scrum framework. Moreover, adopting such management systems can alleviate some of the general difficulties of scientific software engineering, such as interdisciplinary communication, creating sustainable software without relying on external code, and constrained resources and timelines. These emergent and iterative frameworks can additionally support the need for rapid results and ever-changing requirements of the scientist user-group community. This case study indicates that a collaborative development approach centered on an Agile Scrum framework can benefit both the scientific user-group and the software developer team while mitigating some of the difficulties facing the scientific software engineering community.

AUTHOR CONTRIBUTIONS

The alphabetic-order author list reflects a variety of contributions from members in the SCiMMA and SNEWS organizations. Particular contributions to this paper and the SCiMMA-SNEWS collaboration are noted as follows. BC and ALB made primary contributions to the text and led the demonstrations after each phase of development. BC organized and led the development sprints, supported software development during Phases 1 and 2, and implemented the software on cloud infrastructure. ALB served as a SNEWS product owner, supported software development during Phases 0, 1 and 2, and contributed substantially during development sprints. YX led the software development process during Phase 0. PG and YX led the software development during Phases 1 and 2, and contributed substantially during development sprints. MWL supported software development during Phases 1 and 2, and implemented the software on prototype infrastructure. AH served as a SNEWS product owner and provided substantial input during development sprints. AB, AH, MJ, RFL, CDT and RW each provided substantial input during progress reviews after each phase. AB, MJ, and CDT proposed the initial collaboration at a National Science Foundation “Harnessing the Data Revolution” grant proposal meeting.

The SCiMMA Agile Scrum team (AB, DC, BC, VE, SE, PG, DAH, MJ, WL, CM, SN, DP, RT, CW, and RW) supported core SCiMMA software development prior to and during the collaboration. Additional SCiMMA members (MWGJ, CK) have continued support of the SCiMMA project. The SNEWS Signal Prediction, Alert Formation, and Follow-up working group members (ALB, SYB, WB, MC, AC, MCM, ADO, DD, AGR, SG, AH, SH, JPK, AK, VK, ML, RFL, SL, ML, MWL, JM, DM, RN, EO, BWP, NJ, AR, JR, JCLT, CDT, CFV, CJV, LW, XJX, YX) supported SNEWS software development prior to and during the collaboration.

ACKNOWLEDGMENTS

This work is supported by the National Science Foundation “Windows on the Universe: The Era of Multi-Messenger Astrophysics” program: “WoU-MMA:

Collaborative Research: A Next-Generation Super-Nova Early Warning System for Multimessenger Astronomy” through grants 1914448, 1914409, 1914447, 1914418, 1914410, 1914416, 1914426; and via the “HDR-Harnessing the Data Revolution” program, grant 1940209; and with the “Office of Advanced Cyberinfrastructure” through grant 1934752.

-
- [1] J. E. Hannay *et al.*, How do scientists develop and use scientific software?, in *Proceedings of the 2009 ICSE Workshop on Software Engineering for Computational Science and Engineering*, SECSE '09 (IEEE Computer Society, USA, 2009) p. 1–8.
- [2] Z. Merali, Computational science: ...Error, *Nature* **467**, 775 (2010).
- [3] D. Chawla, The unsung heroes of scientific software, *Nature* **529**, 115 (2016).
- [4] F. P. Brooks, The Computer Scientist as Toolsmith II, *Commun. ACM* **39**, 61–68 (1996).
- [5] G. Wilson *et al.*, Best Practices for Scientific Computing, *PLOS Biology* **12**, 1 (2014).
- [6] D. F. Kelly, A Software Chasm: Software Engineering and Scientific Computing, *IEEE Software* **24**, 120 (2007).
- [7] T. Storer, Bridging the Chasm: A Survey of Software Engineering Practice in Scientific Programming, *ACM Computing Surveys* **50**, 1 (2017).
- [8] J. Segal and C. Morris, Developing software for a scientific community: Some challenges and solutions, *Handbook of Research on Computational Science and Engineering: Theory and Practice* (2011).
- [9] K. M. Beck *et al.*, Manifesto for Agile Software Development (2013), <https://agilemanifesto.org>.
- [10] D. Kane *et al.*, Agile methods in biomedical software development: A multi-site experience report, *BMC bioinformatics* **7**, 273 (2006).
- [11] Ž. Ivezić *et al.* (LSST), LSST: from Science Drivers to Reference Design and Anticipated Data Products, *Astrophys. J.* **873**, 111 (2019), arXiv:0805.2366 [astro-ph].
- [12] S. Al Kharusi *et al.* (SNEWS), SNEWS 2.0: A Next-Generation SuperNova Early Warning System for Multimessenger Astronomy (2020) arXiv:2011.00035 [astro-ph.HE].
- [13] K. Schwaber, *Business Object Design and Implementation*, edited by J. Sutherland, C. Casanave, J. Miller, P. Patel, and G. Hollowell (Springer London, London, 1997) pp. 117–134.
- [14] M. Sletholt *et al.*, A Literature Review of Agile Practices and Their Effects in Scientific Software Development, *Proceedings - International Conference on Software Engineering* 10.1145/1985782.1985784 (2011).
- [15] J. Segal, Models of scientific software development, in *SECSE 08, First International Workshop on Software Engineering in Computational Science and Engineering* (2008) workshop co-located with ICSE 08 <http://oro.open.ac.uk/17673/>.
- [16] J. Segal, When Software Engineers Met Research Scientists: A Case Study, *Empirical Software Engineering* **10** (2005).
- [17] C. A. Crabtree, A. G. Koru, C. Seaman, and H. Erdogmus, An empirical characterization of scientific software development projects according to the Boehm and Turner model: A progress report, in *2009 ICSE Workshop on Software Engineering for Computational Science and Engineering* (2009) pp. 22–27.
- [18] M. Umarji *et al.*, Software Engineering Education for Bioinformatics, in *2009 22nd Conference on Software Engineering Education and Training* (2009) pp. 216–223.
- [19] P. Antonioli *et al.*, SNEWS: The Supernova Early Warning System, *New J. Phys.* **6**, 114 (2004), arXiv:astro-ph/0406214.
- [20] K. Nakamura *et al.*, Multi-messenger signals of long-term core-collapse supernova simulations : synergetic observation strategies, *Mon. Not. Roy. Astron. Soc.* **461**, 3296 (2016), arXiv:1602.03028 [astro-ph.HE].
- [21] B. P. Abbott *et al.*, Multi-messenger Observations of a Binary Neutron Star Merger, *Astrophys. J. Lett.* **848**, L12 (2017), arXiv:1710.05833 [astro-ph.HE].
- [22] M. J. Graham *et al.*, The Zwicky Transient Facility: Science Objectives, *Publ. Astron. Soc. Pac.* **131**, 078001 (2019), arXiv:1902.01945 [astro-ph.IM].
- [23] M. Smith *et al.*, The Astrophysical Multimessenger Observatory Network (AMON), *Astropart. Phys.* **45**, 56 (2013), arXiv:1211.5602 [astro-ph.HE].
- [24] M. Ageron *et al.*, The ANTARES Telescope Neutrino Alert System, *Astropart. Phys.* **35**, 530 (2012), arXiv:1103.4477 [astro-ph.IM].
- [25] E. Huerta *et al.*, Enabling real-time multi-messenger astrophysics discoveries with deep learning, *Nature Rev. Phys.* **1**, 600 (2019), arXiv:1911.11779 [gr-qc].
- [26] M. G. Aartsen *et al.* (IceCube), The IceCube Real-time Alert System, *Astropart. Phys.* **92**, 30 (2017), arXiv:1612.06028 [astro-ph.HE].
- [27] International Astronomical Union, The Transient Name Server, <https://www.wis-tns.org/> (2015).
- [28] S. D. Barthelmy *et al.*, GRB Coordinates Network (GCN): A status report, *AIP Conference Proceedings* **526**, 731 (2000), <https://aip.scitation.org/doi/pdf/10.1063/1.1361631>.
- [29] R. D. Williams and R. Seaman, *Astronomical Data Analysis Software and Systems XV*, edited by C. Gabriel, C. Arviset, D. Ponz, and S. Enrique, *Astronomical Society of the Pacific Conference Series*, Vol. 351 (2006) p. 637, <https://ui.adsabs.harvard.edu/abs/2006ASPC..351..637W>.
- [30] R. Rutledge, The Astronomer’s Telegram: A Web-based Short-Notice Publication System for the Professional Astronomical Community, *Publ. Astron. Soc. Pac.* **110**, 754 (1998), arXiv:astro-ph/9802256.
- [31] P. Chang *et al.*, Cyberinfrastructure Requirements to Enhance Multi-messenger Astrophysics (2019), arXiv:1903.04590 [astro-ph.IM].

- [32] SCiMMA Collaboration, Scimma google groups, <https://groups.google.com/g/scimma> (2020).
- [33] SCiMMA Collaboration, Scimma virtual workshop, <https://scimma.org/events/virtual2020> (2020).
- [34] P. Godwin *et al.*, scimma/hop-client: v0.2 release of scimma/hop-client, <https://doi.org/10.5281/zenodo.4033483> (2020).
- [35] SCiMMA Collaboration, Scimma infrastructure repository, <https://github.com/scimma/scimma-admin> (2020).
- [36] M. A. Heroux and J. M. Willenbring, Barely Sufficient Software Engineering: 10 Practices to Improve Your CSE Software, in *Proceedings of the 2009 ICSE Workshop on Software Engineering for Computational Science and Engineering*, SECSE '09 (IEEE Computer Society, USA, 2009) p. 15–21.
- [37] SCiMMA Collaboration, Scimma containerization repository, <https://github.com/scimma/scimma-server-container> (2020).
- [38] DIDACTS Collaboration, Data-intensive discovery accelerated by computational techniques for science, <https://didacts.org> (2020).
- [39] National Science Foundation, Harnessing the data revolution at nsf, <https://www.nsf.gov/cise/harnessingdata/> (2020).
- [40] M. J. Sax, Apache kafka, in *Encyclopedia of Big Data Technologies* (Springer International Publishing, Cham, 2018) pp. 1–8, https://doi.org/10.1007/978-3-319-63962-8_196-1.
- [41] A. Depoian, Using SCiMMA architecture for SNEWS 2.0, <https://www.youtube.com/watch?v=GJLTCycvknE> (2020).
- [42] R. Pope-Ruark, Introducing Agile Project Management Strategies in Technical and Professional Communication Courses, *Journal of Business and Technical Communication* **29**, 112 (2015), <https://doi.org/10.1177/1050651914548456>.
- [43] B. Cousins and A. Depoian, SNEWS 2.0 Prototyping with SCiMMA, <https://www.youtube.com/watch?v=ZZ04CIqUTcY> (2020).
- [44] P. Godwin *et al.*, SNEWS2/hop-SNalert-app: Release 1.0 For Zenodo reference, <https://doi.org/10.5281/zenodo.4437579> (2021).
